Oringal tile and all ties destroyed by road construction. Set 5/8" Iron Pin in line with property Line fence west and on centerline of road. 4/15/99
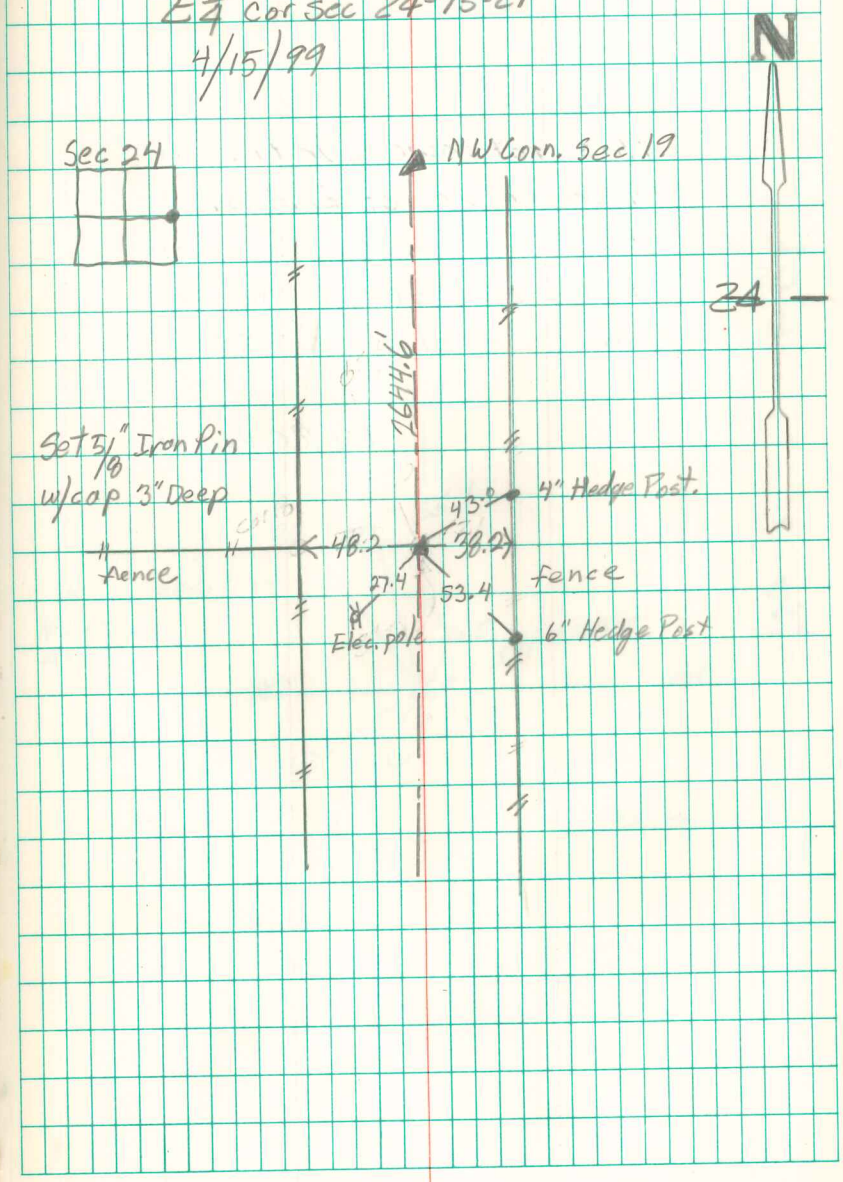
E¼ cor Sec 24-75-21
4/15/99
